


The Client
NEWSLETTER

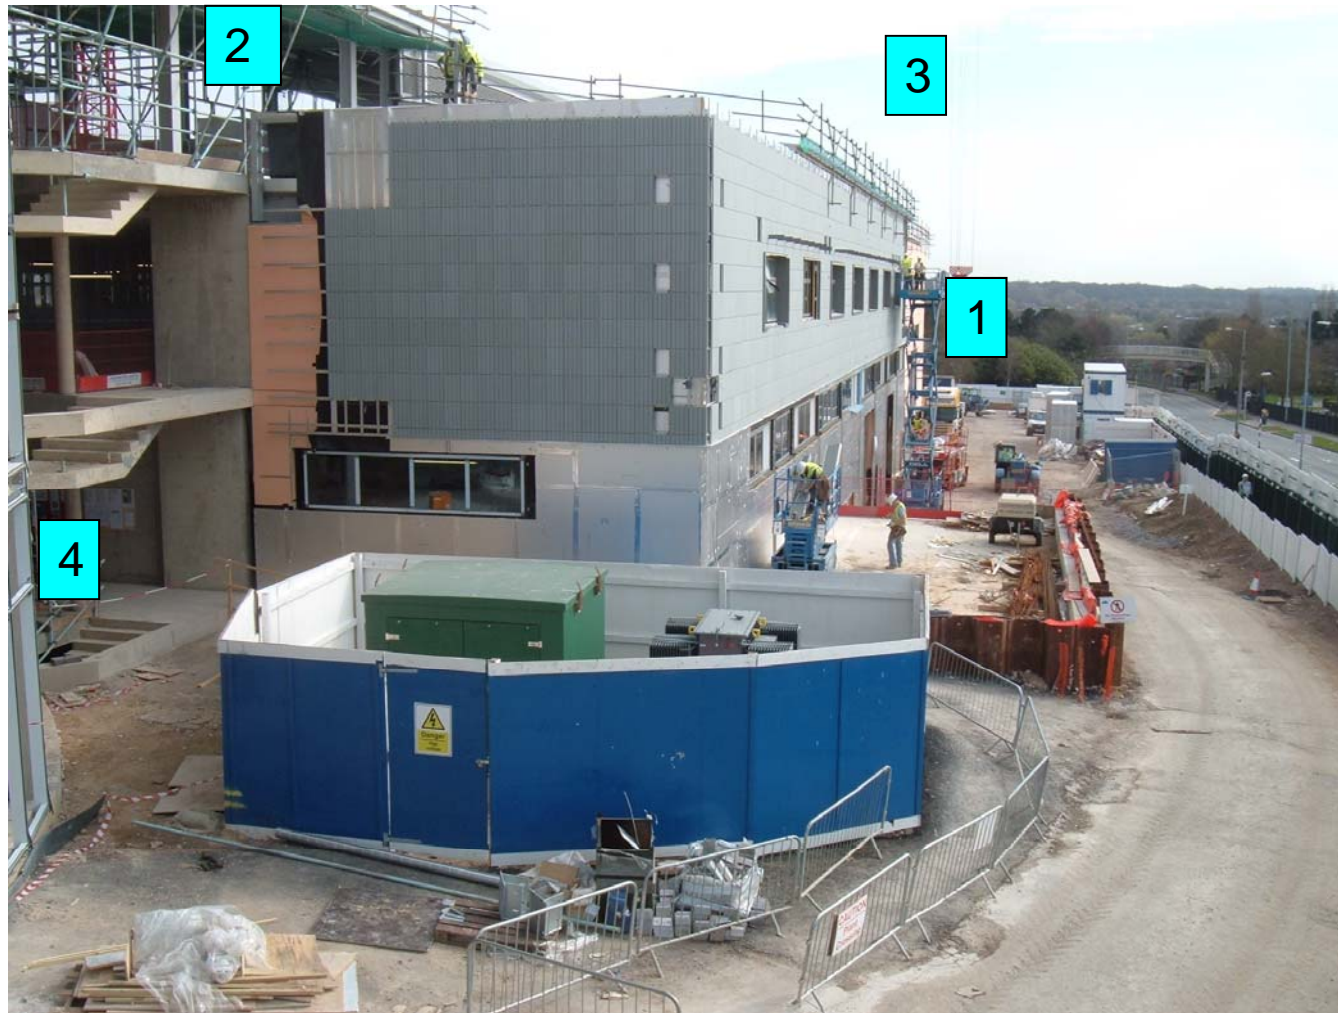

Operations in picture:

1. Window pod and solar shading brackets being installed.
2. Block E and D link access being installed to enable the roof to be completed.
3. Plant being lifted into the plant areas located in Blocks C and D
4. External glazing system commenced to Block E.

Other operations:

1. External wall infill panels to Block C.
2. M&E first fix operations continue to Block D.
3. Plaster boarding of walls and plastering of walls continues to Block D levels 2 and 1.

Moving forward:

Pushing on with getting the blocks weather tight to allow the internal trades to commence in areas as they are released

9th April 2010

Blocks D & C

29th Edition



Operations in picture:

1. The laminated wood beams (Glulam) being installed to the roof area of Block E
2. The external glazed walls (Curtain walling) being installed to Block E

Other operations:

1. Roof coverings being installed to Blocks F and G.
2. External wall tiling being installed to the street side of Block F
2. M&E first fix operations continue to Blocks F & G .
3. Plaster boarding of walls to Blocks F & G Levels 2 and 1

Moving forward:

Pushing on with getting the blocks weather tight to allow the internal trades to commence in areas as they are released
